




M.E. SIMPSON COMPANY, INC.

LEAK LOCATION REPORT

Client: Aurora, Illinois **Time:** 9:30 AM
Date: December 22, 2025 **Tech:** Sandison P. & Juan M.
Address: Ohio Street & Indian Avenue (N. of)

Below is a diagram of the area surveyed for a suspect leak.

This drawing is not to scale.

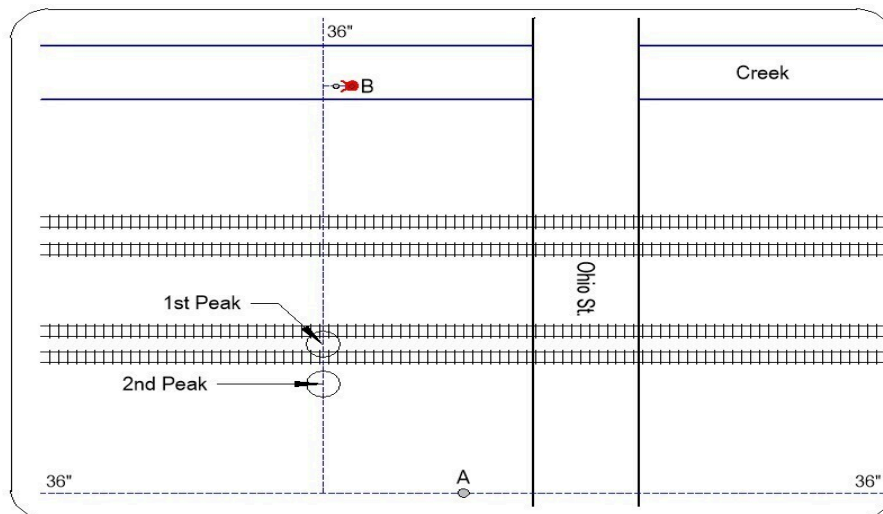

Distance: 380' from A to B
Connection point: A= Main Line Valve **Connection point:** B= Hydrant
Leak Location: 240' from A
Comments: This is a leak on a 36" main. We came up with two peaks. The first was 240' from "A", and the second was 210' from "A". The first peak was the strongest. "B" is missing its head and is in the creek.

*We thank you for the opportunity to work for your Utility and look forward to serving you again.
If you have any questions please don't hesitate to call.*
